UPPER TRISHULI-1 HEP (216MW)

Client	**Nepal Water and Energy Development Company Private Limited**
Owner's Engineer	**Tractebel Engineering GmbH / Jade Consult**

REVIEW NOTE

Contractor	**Doosan Heavy Industries & Construction Co., Ltd.**		
Title of the Document	Layout Drawing for Monitoring of Main Access Tunnel		
Document No.	UT1-C-845-CVL-DG-70007	Revision	0A
Date of Documents	05.01.2022	Received Date	09.01.2022
Transmittal Form No.	UT1-HEP-DHI-D-0113		
Previous Review Date/Status	N/A	Prev. Review Note No.	N/A
Review Note No.	**RN-0096**	**Present Review Date**	**26.03.2022**
		Present Review Status	**RR**

A: Approved AN: Approved as Noted RR: Returned for Resubmission FI: For Information, only

The document was received as pdf-file. To simplify the review by the Engineer and to assist the Contractor in the revision, drawings of the pdf-file were copied into this review note and marked with red letters, and corrections were suggested.

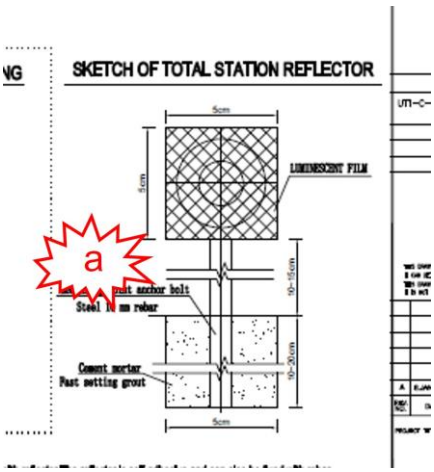

a) Distance between rock surface and target should be "max. 30 mm" and not "10 cm – 15 cm".

The tunnel encounters two junctions. Respective monitoring system shall be developed for both junctions for the individual construction stages of the junctions.

DISCLAIMER

Any approval will not release the Contractor from any of his obligations under the Contract.

Dr. Ulrich Glawe
